Arkansas Department of Health
Environmental Health Protection

Receipt Number: 28894082

Individual Onsite Wastewater System Permit Application

Permit Type: ☒ New Installation ☐ Alteration / Repair

DR Environmental ID #: 7 6 0 2 1 3 2 0 9 0

Fee Schedule for Structures		√
Structures 1500 sq ft or less	$ 30.00	☐
Structures more than 1500 sq ft and up to 2000 sq ft	$ 45.00	☐
Structures more than 2000 sq ft and up to 3000 sq ft	$ 90.00	☒
Structures more than 3000 sq ft and up to 4000 sq ft	$120.00	☐
Structures more than 4000 sq ft	$150.00	☐
Alteration and Repair	$ 30.00	☐

Part 1 Application

Treatment Type (check one)
- ☒ STD = Standard Septic Tank
- ☐ ISF = Intermittent Sand Filter
- ☐ PMF = Proprietary Media Filter
- ☐ OTH = Other (Describe)
- ☐ ATU = Aerobic Treatment Plant
- ☐ RSF = Re-circulating Sand Filter
- ☐ RGF = Re-circulating Gravel Filter
- ☐ HLD = Holding Tank

Disposal Method (check one)
- ☒ STD = Standard Absorption Field
- ☐ SUR = Surface Discharge
- ☐ CPF = Capping Fill
- ☐ OTH = Other
- ☐ LPD = Low Pressure Distribution
- ☐ HLD = Holding Tank
- ☐ SRL = Serial Distribution
- ☐ DRP = Drip Irrigation

1. Owner's/Applicant's Name BRANDON GRANT	2. Phone Number KENNEDY 501-626-6202
3. Mailing Address BRAGGCONSTRUCTION@YAHOO.COM	4. County PULASKI

5. Address of Proposed System (If a 911 address is not available, attach detailed directions or map)
510 STEWART RD. LITTLE ROCK, AR. 72211

6. Subdivision Name KENNEDY ESTATES	7. Approval Date NONE	8. Date Recorded NONE	9. Lot Number 1
10. Lot Dimensions SEE LEGAL	11. Total Area (Acres) 4.76	12. # Bedrooms # People 4	13. Daily Flow (GPD) 450

14. Brief Legal Description of Property (Attach a separate sheet of paper, if necessary)
SECTION- 2 TOWNSHIP - 1-N RANGE- 14-W

15. Water Supply (Specify supplier, if Public Water) CENTRAL ARKANSAS WATER	16. GPS Coordinates 34.758980, -92.476220

17. Loading Rates	(gpd/ft²)	18. System Specifications						
Primary Area	.49	a. Size of Septic Tank	1250	gal	f. Trench Depth	18	inches	
Secondary Area	N/A	b. Size of Dose Tank	250	gal	g. Trench Spacing	10	feet	
Percolation Test	(min/in)	c. Absorption Area	1000	ft²	h. Trench Media (List Below)		i.Trench Width	
Primary Area Avg	X	d. Number of Field Lines	4		EZ FLOW 1201		12/18	in
Secondary Area	X	e. Length of Field Lines	125	ft	CHAMBERS		18	in

TO THE OWNER
The permit for construction may be deemed invalid by the local Environmental Health Specialist before the start of construction, if the site and/or soil conditions have changed after approval of this permit, or if the information within this permit is inaccurate or has been found to be misrepresented. Approval for operation does not constitute a guarantee that the system will function properly. The approval states that the system was designed and installed according to the Arkansas Department of Health, Rules and Regulations Pertaining to Onsite Wastewater Systems, unless there are exceptions or deviations noted in the comments. A Permit for Construction is valid for one (1) year from the date of approval. The authorized agent must revalidate a permit more than one (1) year old prior to the start of any construction.

19. Utilization Verification
I hereby attest that item 12, the number of bedrooms (number of persons for commercial) and square footage of the structure that will utilize the designed individual onsite wastewater system in this permit application, is accurate. I have reviewed the permit application and understand the layout, installation, maintenance, operation and expense(s) that may be associated with this system.

Owner/Applicant Signature _____ Date _____

20. I certify that I have conducted the above tests and that the above listed information is in accordance with the latest requirements of the Arkansas Department of Health Rules and Regulations Pertaining to Onsite Wastewater Systems.

Designated Representative Signature | D.R. Title | Soil Certified ☒ Yes ☐ No

KEVIN CASTLEBERRY (Print Name) | 11/8/2026 (Date) | 870-692-5742 (Phone Number)

21. Approval of Health Authority
The information and specifications in the application has been reviewed and found to meet the requirements of the Arkansas Department of Health Rules and Regulations Pertaining To Onsite Wastewater Systems. A PERMIT FOR CONSTRUCTION is hereby issued.

Environmental Specialist Signature | 302 (EHS Number) | 11-10-26 (Date)

Individual Onsite Wastewater System Permit Application

Receipt Number

Continue Part 1

22. Soil Criteria (Primary Area)			Indicate the depth to items a-f, if observed in the soil (designate in inches)				
a. Bedrock	b. BSWT	c. MSWT	d. LSWT	e. Adj. MSWT	f. Adj. LSWT	g. H.C./Depth	h. Loading Rate (gpd/ft^2)
X	22	24	X	23	X	M-48	.49

23. Soil Criteria (Secondary Area)			Indicate the depth to items a-f, if observed in the soil (designate inches)				
a. Bedrock	b. BSWT	c. MSWT	d. LSWT	e. Adj. MSWT	f. Adj. LSWT	g. H.C./Depth	h. Loading Rate (gpd/ft^2)
X	12	17	X	15	X	M-48	ATU SURF. DISCHARGE

24. Seasonal Water Table (SWT) Classes Detail

Primary Area			List Redoximorphic Features and/or Clay Content Restrictions
Brief	22	in	2.5 YR 5/8
Moderate	24	in	10YR 6/2
Long	X	in	10 YR 6/2 > 50%
Secondary Area			**List Redoximorphic Features and/or Clay Content Restrictions**
Brief	12	in	2.5 YR 5/8
Moderate	17	in	10YR 6/2
Long	X	in	10 YR 6/2 >50%

Comments

Part 2 Installation Inspection

Septic tank manufacturer	Pump information
Septic tank material	Trench media and width
Dose tank manufacturer	Depth of interceptor drain
Dose tank material	Depth of settled fill

Name of Installer	License Number

Installation Inspected by ☐ Environmental Health Specialist ☐ Designated Representative
(check one or installer signs System Installation Verification below)

Signature _____ EHS / License Number _____ Date _____

System Installation Verification
I have installed this system as designed and in compliance with all Rules and Regulations Pertaining to Onsite Wastewater Systems.

Installer Signature _____ License Number _____ Date _____

Part 3 Permit for Operation


The information contained in Part 1 and 2 of this form has been reviewed and found to meet the requirements of the Arkansas Department of Health. THE PERMIT FOR OPERATION of this system is hereby issued.

Environmental Health Specialist _____ Signature _____ EHS Number _____ Date _____

Comments

Site Revalidation conducted by ☐ Environmental Health Specialist ☐ Designated Representative
(check one)

Signature _____ EHS / License Number _____ Date _____

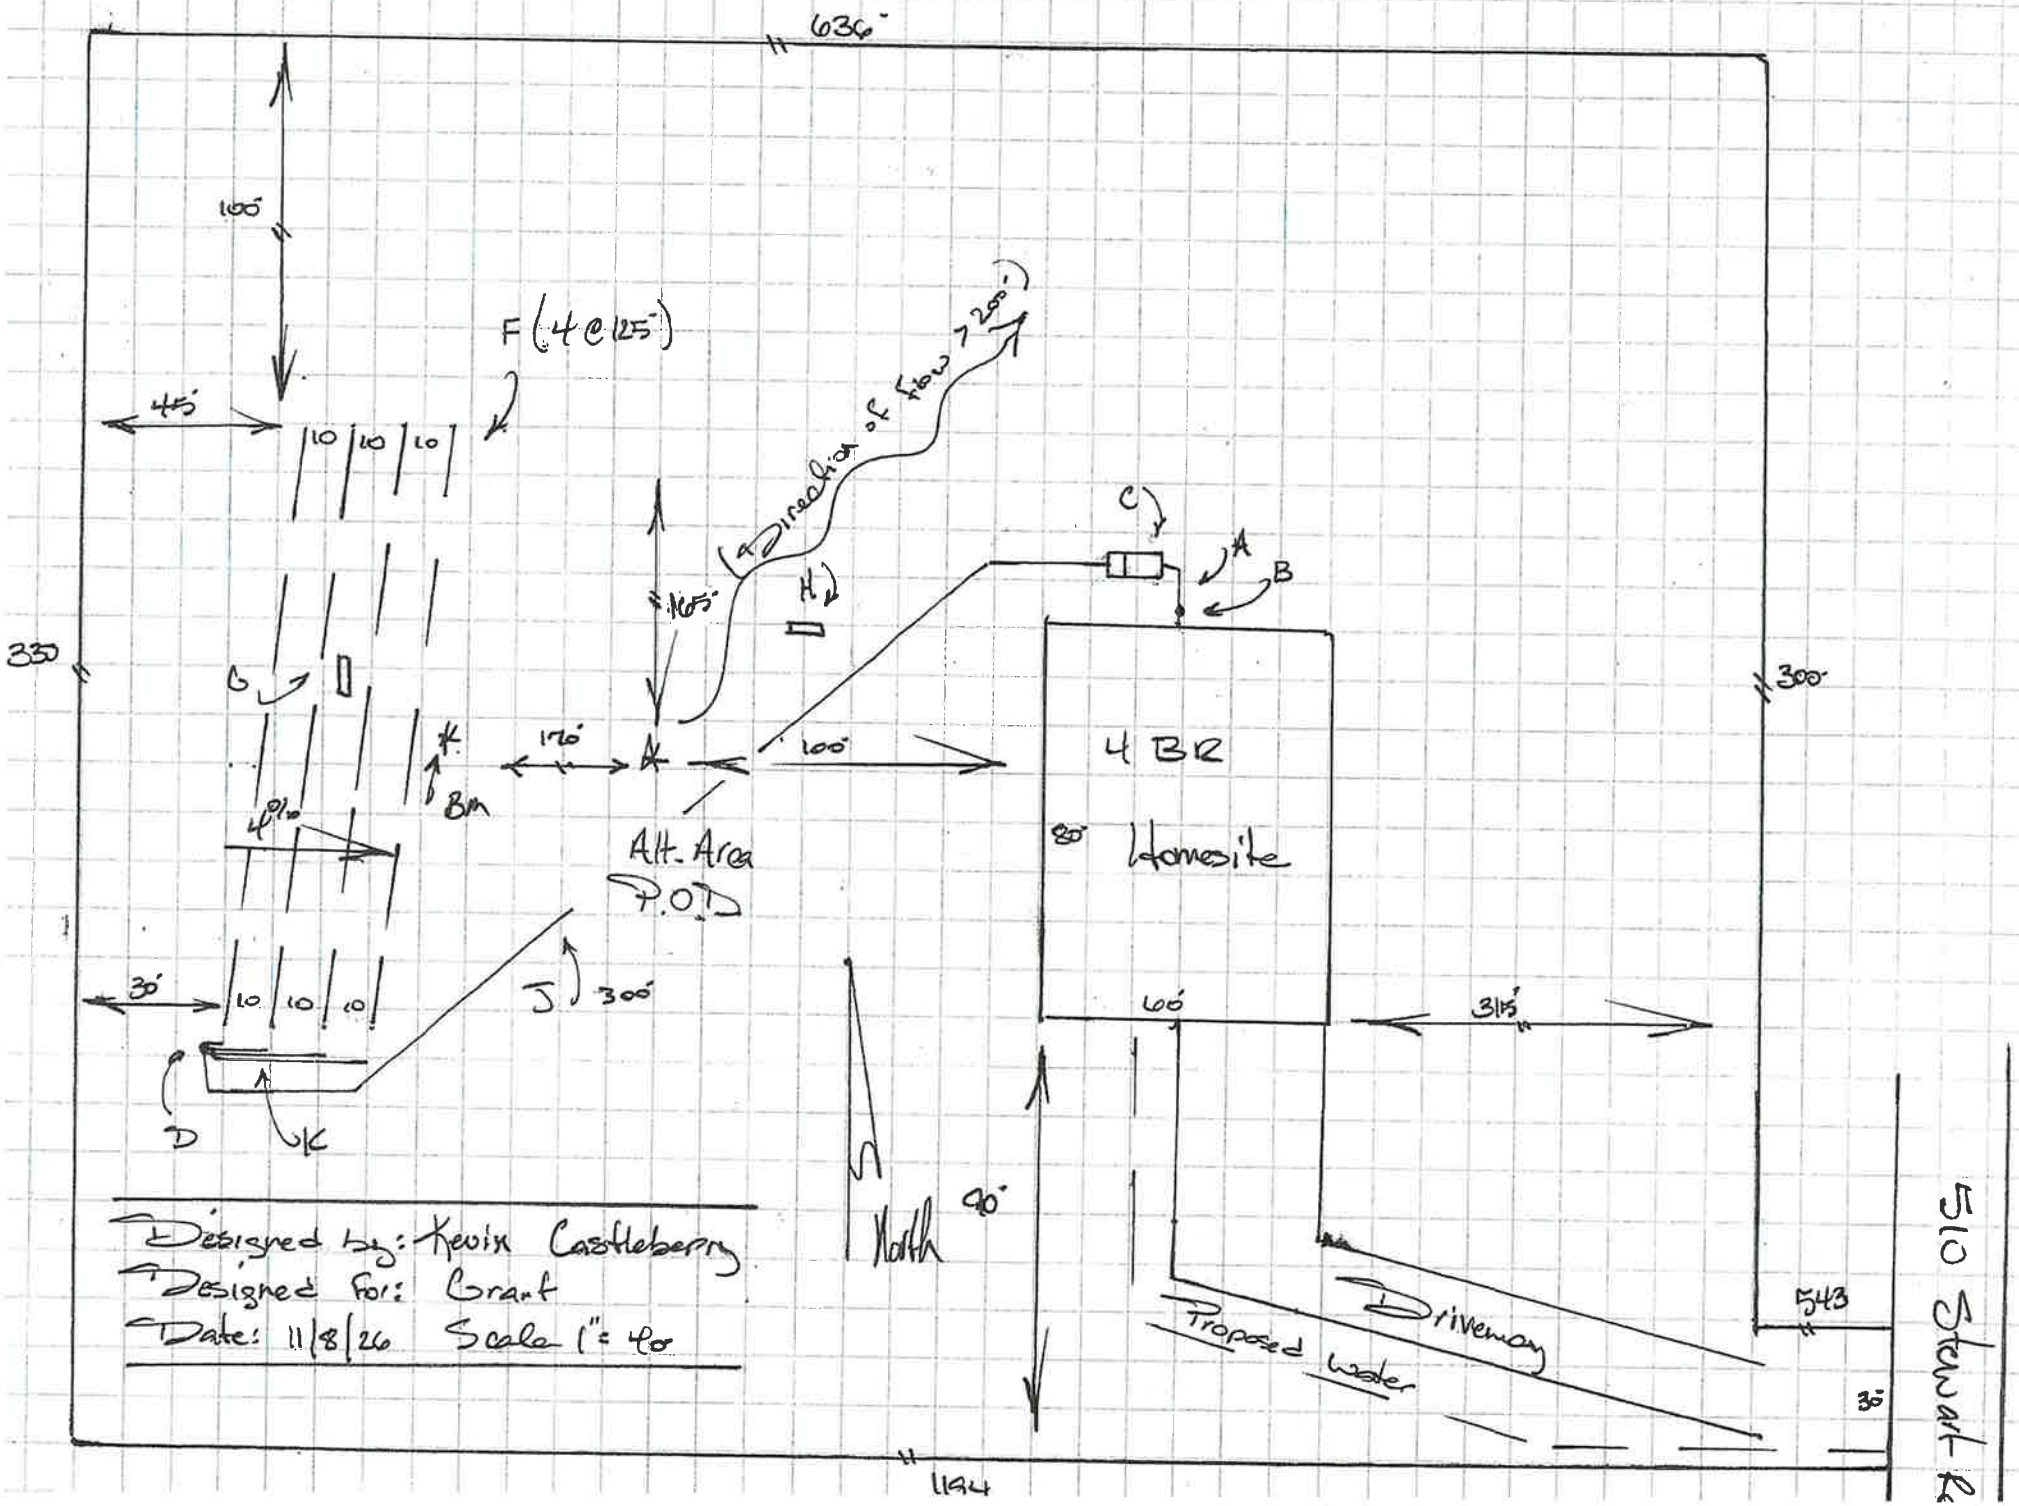

Designed by: Kevin Castleberry
Designed for: Grant
Date: 11/8/26 Scale 1" = 40'

APPLICANT:	BRANDON GRANT

ELEVATIONS

	GROUND ELEV.	FLOW LINE ELEV.
BENCHMARK:	3.6	
STUB OUT:	8.5	9.5
CLEAN OUT:	8.5	9.5
TANK IN:	8.5	9.7
TANK OUT:	8.5	9.10
PUMP INTAKE:	8.5	12.10
PRES. MAN.	2.0	2.6

LINE #	BEG	MID	END	TRENCH BOTTOM	TRENCH DEPTH	LINE LENGTH
#1	2.3	2.3	2.3	3.9	18	125
#2	2.11	2.11	2.11	4.5	18	125
#3	3.2	3.2	3.2	4.8	18	125
#4	3.6	3.6	3.6	5.0	18	125
#5						
#6						
#7						
CURT. DRAIN						
A1	POD	9.0				
A2						
A3						
A4						
A5						

LEGEND:

(A) 4" SCH. 40 PIPE
(B) 4" CLEAN OUT AND PLUG
(C) SEPTIC TANK
(D) PRESSURE MANIFOLD
(E) 4" SDR 35
(F) FIELD LINE LATERALS
(G) PIT #1
(H) PIT #2
(I) 2" SCH. 40
(J) 1½" SCH. 40
(K) ¾" SCH 40

NOTES:

SEPTIC TANK

1. INSTALL *1250/250-GALLON* TANK. (BOTTOM OF HOLE MUST BE FIRM AND GRADED LEVEL)
2. SEPTIC TANK MUST HAVE MINIMUM 16" DIAMETER RISERS OVER THE INLET AND OUTLET BAFFLES AND MINIMUM 20" DIAMETER RISER OVER THE PUMP CHAMBER. EXTEND ALL RISERS ABOVE NATURAL GROUND ELEVATION. APPLY ¼" BUTYL SEALANT BETWEEN ALL RISER EXTENSIONS.
3. INSTALL OUTLET FILTER IN THE OUTLET BAFFLE OF THE SEPTIC TANK. (SEE SPEC SHEET).

PUMP/ALARM

1. INSTALL ZOELLER *BN 151* PUMP, SET ON TWO 8X8X16 CONCRETE BLOCKS.
2. PLUMB PUMP WITH 1 ½" SCH 40 PIPE THROUGH THE RISER USING A 1 ½" POLYLOK GROMMET. (DO NOT USE THE BOOT SEAL CAST INTO TANK, UNLESS BOOT IS DESIGNED TO FIT 1 ½" PIPE)
3. PLUMBING SHOULD INCLUDE:
    A. 1 ½" CHECK VALVE
    B. 1 ½" UNION
    C. 1 ½" BALL VALVE
4. SET PUMP FLOAT SWITCH WITH *3.5"* TETHER LENGTH. THIS WILL PUMP APPROXIMATELY *50* GALLONS PER DOSE. PUMP SHOULD STAY SUBMERGED IN WATER WHEN SWITCH IS IN OFF POSITION.
5. INSTALL SPI 508137 CONTROL PANEL.
6. ALARM FLOAT SHOULD BE POSITIONED ABOVE THE ON POSITION OF THE PUMP FLOAT. TETHER ON ALARM FLOAT SHOULD BE POSITIONED SO THE ALARM SOUNDS BEFORE THE WATER LEVEL IN THE PUMP CHAMBER RISES INTO THE OUTLET PIPE OF THE SEPTIC TANK.
7. PUMP AND ALARM MUST BE ON SEPARATE BREAKERS.
8. ALL ELECTRICAL CONNECTIONS SHOULD BE MADE IN WATERPROOF SPLICE BOX WITH CORD GRIPS. (SEE SPEC SHEET)
9. USE PIPE SEAL/GROMMET FOR ELECTRICAL CONDUIT. CONDUIT SHOULD EXIT THROUGH RISER.

ABSORPTION AREA:

1. INSTALL 1 ½" X ½" X ¾" PRESSURE MANIFOLD WITH ½" UNIONS AND 24" OF ¾" SPA TUBING ON EACH LINE. CONTINUE WITH RIGID ¾" SCH 40 TO THE BEGINNING OF EACH LINE. INSTALL PLASTIC ORIFICE DISK IN EACH UNION AS SPECIFIED ON SPIDER VALVE SIZING SHEET. COVER MANIFOLD WITH VALVE BOX, OR RISER EXTENSION AND LID.
2. FIELD LINES CONSIST OF *(4-125')* LINES ON *10'* CENTERS, OR AS MARKED WITH 18" DEEP TRENCHES.
3. INSTALLER MAY USE TRENCH MEDIA LIST ON EHP-19 (18H). SEE MANUFACTURER'S INSTALLATION INSTRUCTIONS.

CLARUS ENVIRONMENTAL

Zoeller Company

ZOELLER PUMP COMPANY

System Head Curve and Pump Selection Tool

Static Head Information	
Static Head - elevation difference from low water to outfall	10.0 feet
System high point above outfall?	No

Friction Head Information	
Pipe	
How many different pipes in the system (not counting laterals)?	1
Pipe 1 Length	300 feet
Pipe 1 Size	1 1/2 inches
Pipe 1 Class	SCH 40
Pipe 2 Length	
Pipe 2 Size	
Pipe 2 Class	
Pipe 3 Length	
Pipe 3 Size	
Pipe 3 Class	
Pressurized Laterals?	No
How many are closed at once?	
Length of one lateral	
Size of lateral	
Class of lateral	


Fittings & Discharge Assemblies

Type	Size	Quantity	Flow
90 Elbow	1 1/2 inches	3	100 %
Check Valve	1 1/2 inches	1	100 %
Discharge Assembly	2 inches		100 %

Special Friction Considerations		
Weep Hole	Yes	1/8 "
Add-In Friction	15 % of Pipe Loss	
Automatic Multizone Valve?	Yes	100 % Total Flow
Pressure Filter?	No	

Operating Head Information		
System Type	Spider Valve	
Required Pressure	3. feet	
Number of Orifices		
Size of Orifices		
	3/8 "	3/8 "
Spider Valve Orifice Sizes (Data originates from Spider Valve Sizing Tab)	3/8 "	3/8 "

Factors and Coefficients	
Hazen-Williams C Factor	130
Discharge Coefficient (Cd)	0.61
Lateral Design Mode	Off

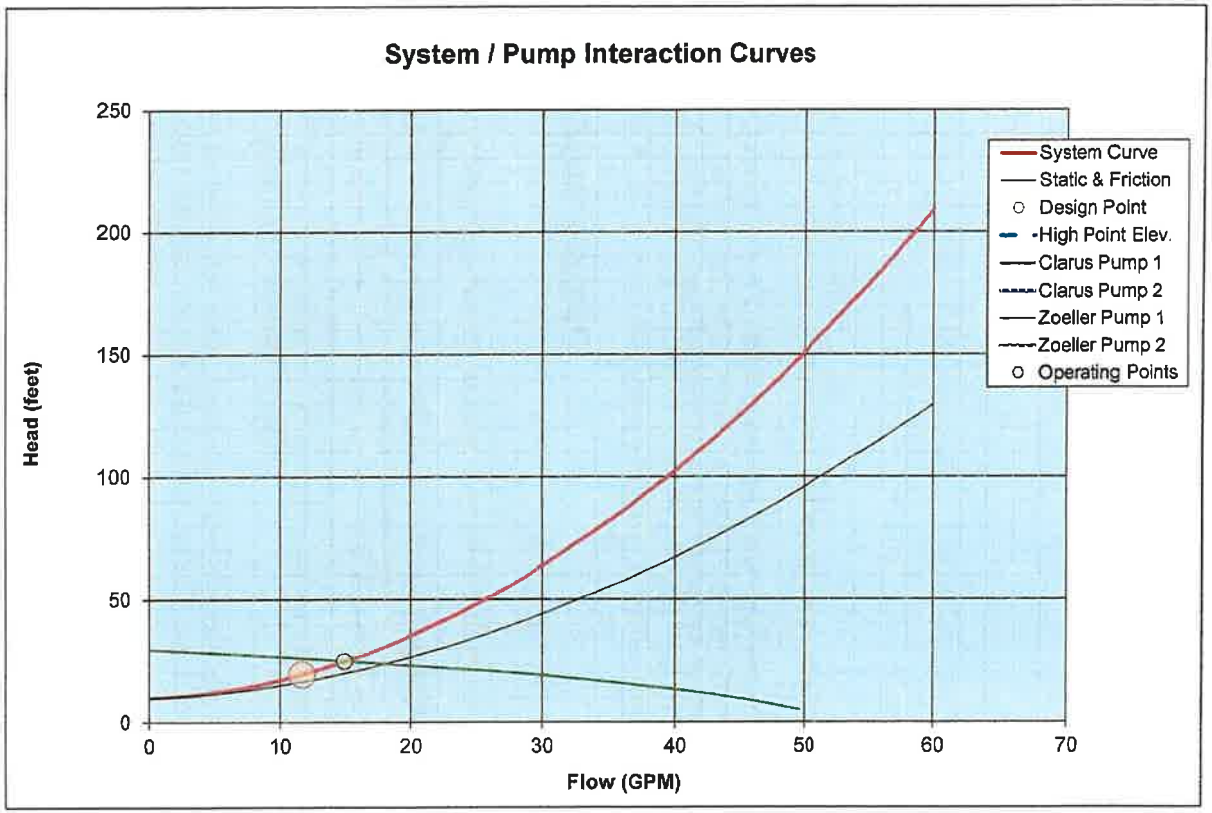

NOTE: THE DISPLAYED PUMP CURVES HAVE BEEN ADJUSTED TO ACCOUNT FOR THE EFFECT OF THE WEEP HOLE

Pump Selection	60 Hz	Frequency	
Clarus Environmental Pumps			Operating Points
Clarus Pump 1			
Flow Control Orifice?			
Clarus Pump 2			
Flow Control Orifice?			
Zoeller Pump Company Pumps			
Zoeller Pump 1	151, 0.3hp, 60Hz		15.0 GPM @ 25.0'
Zoeller Pump 2			

Design Point
11.7 GPM
@ 19.5 ' TDH

Curve Zoom Range	60 GPM

Project Data		Notes:
Project Name:	510	
Project Address		
Contact Info:		

Version 4.51

CLARUS ENVIRONMENTAL

Zoeller Company

Spider Valve Sizing Tool

1-877-244-9340

Number of Outlets	4
Distal Pressure	3 ft
Maximum Orifice	3/8 "

Lateral Line #1	Length	125 ft	Orifice Size	0.369 "	Drill Size	3/8 "
Lateral Line #2	Length	125 ft	Orifice Size	0.369 "	Drill Size	3/8 "
Lateral Line #3	Length	125 ft	Orifice Size	0.369 "	Drill Size	3/8 "
Lateral Line #4	Length	125 ft	Orifice Size	0.369 "	Drill Size	3/8 "

Total Flow
11.67 GPM

Project Data		Notes:
Project Name:	510	
Project Address		
Contact Info:		


The tools and information contained herein are made available for your use. Clarus Environmental and Zoeller Company believe this information to be correct and accurate at the time of issue. However, Clarus Environmental and Zoelller Company assume no liability, expressed or implied, resulting from the access and use of this information. It is solely the responsibility of the user to verify that the information is correct and accurate for the required purposes. Use of this program implies aceptance of, and agreement with, these responsibilities.

Version 4.51


1250 – Gallon Single Compartment W/250 Pump Tank

TOP VIEW


Drawings Not To Scale

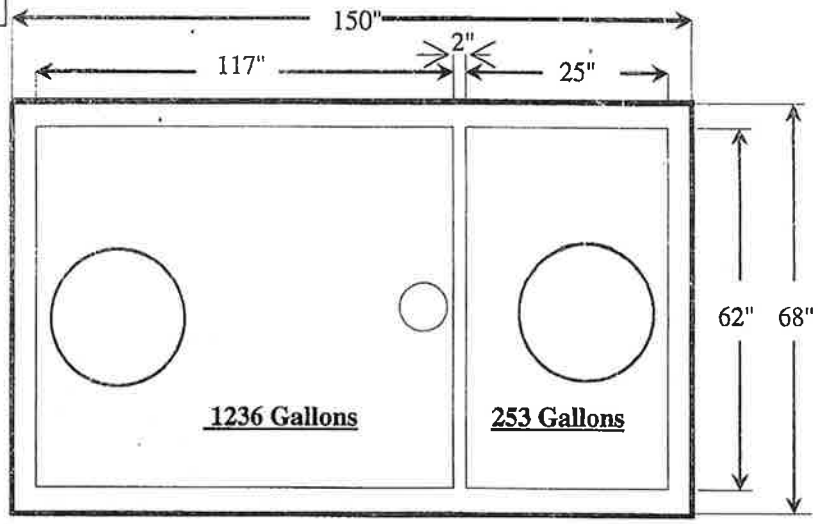


Enlarged Detail

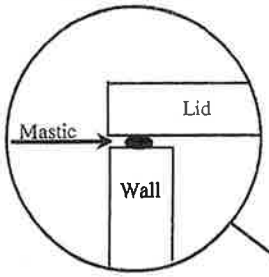

SIDE VIEW

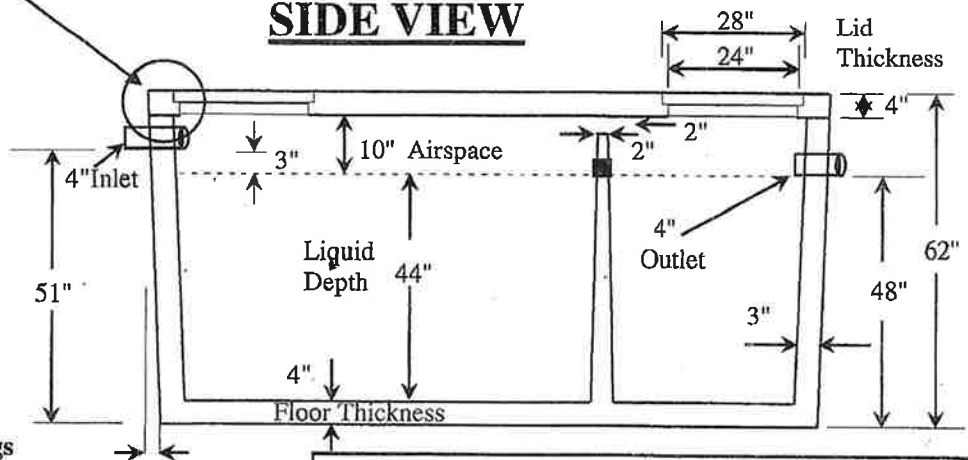


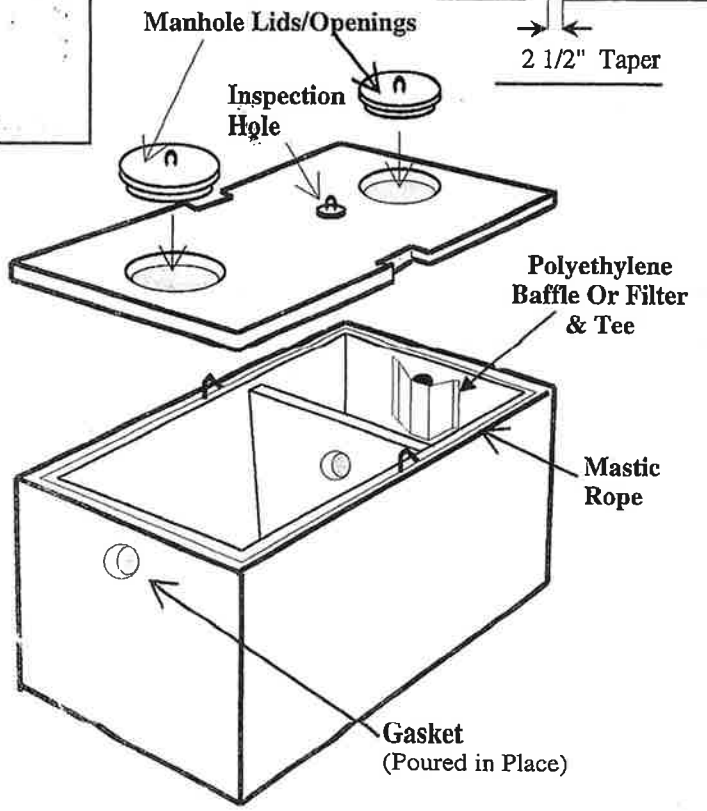



WHITTEN CONCRETE CO.
2703 W. 2nd AVE.
PINE BLUFF, AR. 71601
PHONE: 870-534-6901
FAX: 870-534-6902


1250 - Single Compartment W/250 Pump Tank
Drawing #: DZ-2
Drawing by: SMR **Date: 1/19/2011**

REVISONS			
REV.	DESCRIPTION	DATE	REV BY
A	INITIAL RELEASE	6/17/2014	CTC
B	UPDATED TO CURRENT STANDARDS	4/27/2021	DFB

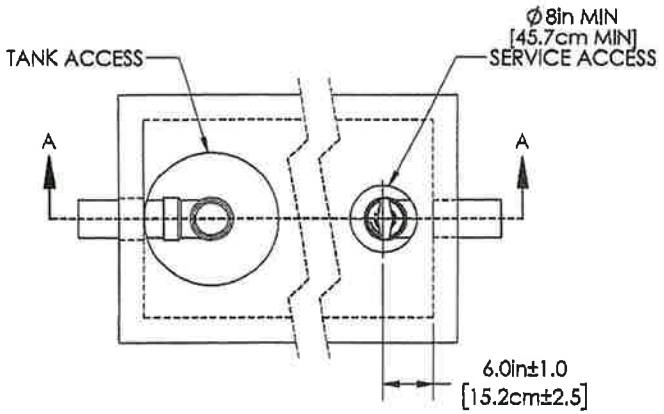


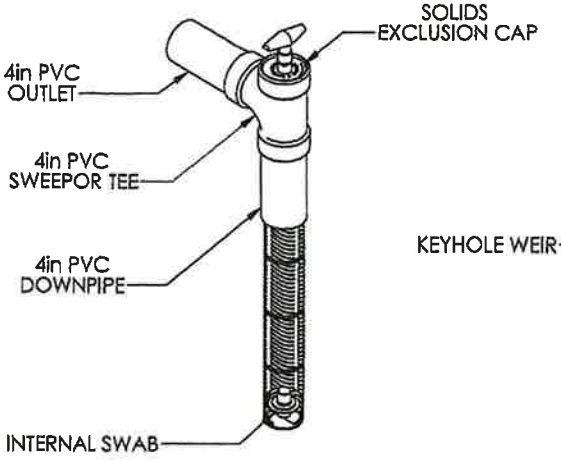

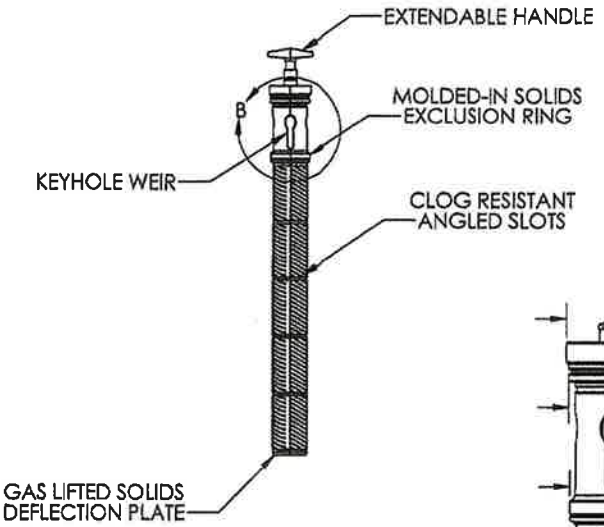


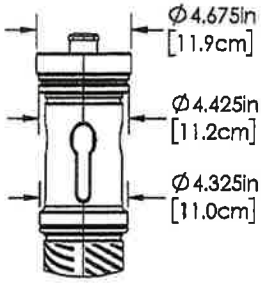

DETAIL B
SCALE 1 : 6

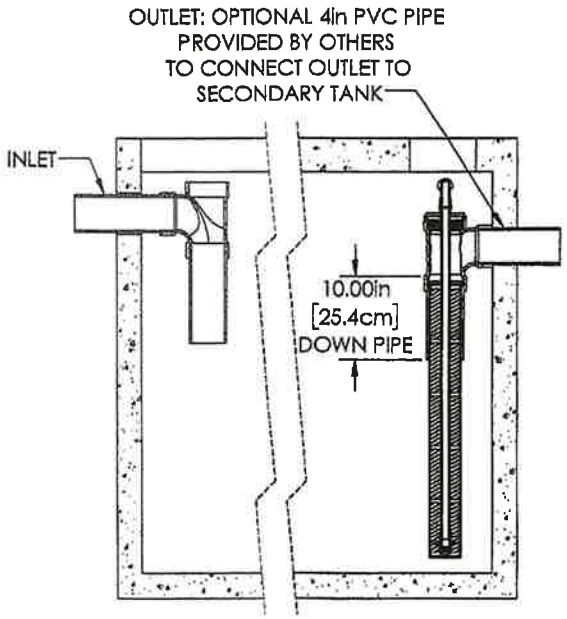

SECTION A-A
SCALE 1 : 15

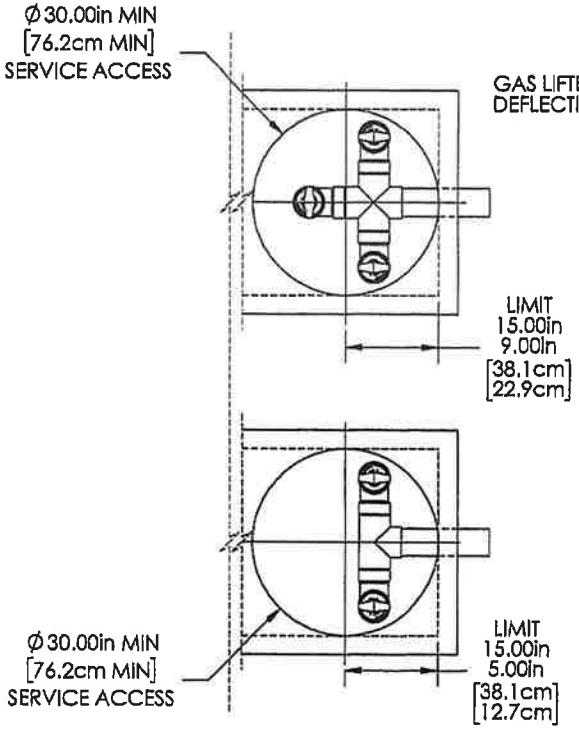

NOTES:

1. SNT 416 IS A 1/16" [1.6MM] EFFLUENT SCREEN CAPABLE OF SCREENING UP TO 1,000 GPD [3.8 CUBIC METERS PER DAY].
2. SNT 418 IS A 1/8" [3.2 MM] EFFLUENT SCREEN CAPABLE OF SCREENING UP TO 2,000 GPD[7.6 CUBIC METERS PER DAY].
3. DOWN PIPE, OUTLET PIPE, AND TEE OR SWEEP NOT INCLUDED.
4. ALL APPURTENANCES TO SANITEE® (E.G. SEPTIC TANK, ACCESS RISERS, ETC.) MUST CONFORM TO ALL APPLICABLE CODES.

PROPRIETARY AND CONFIDENTIAL
THE INFORMATION CONTAINED IN THIS DRAWING IS THE SOLE PROPERTY OF BIO-MICROBICS, INC.. ANY REPRODUCTION IN PART OR AS A WHOLE WITHOUT THE WRITTEN PERMISSION OF BIO-MICROBICS, INC. IS PROHIBITED.
DO NOT SCALE DRAWING

SHEET 1 OF 1

SCALE: N/A | SIZE: B

UNLESS OTHERWISE SPECIFIED
DIMENSIONS ARE IN INCHES AND TOLERANCES ARE AS FOLLOWS
X° ±1°
.X ± .50
.XX ± .25

DRAWN BY: DFB
DATE: 4/27/2021
APPROVED BY: MSH
APPROVED BY DATE: 4/27/2021

BIO MICROBICS
BETTER WATER, BETTER WORLD

DESCRIPTION: 4in SaniTEE®
PART NUMBER: SaniTEE® 416 & 418
REV: B

Nema-4X Junction-boxes

Economy Junction Box (Field Assembled)


PVC plastic box with removable cover for use in sewage, effluent, dewatering, or corrosive environments. Box is 4" x 4"x 2" (10 x 10 x 5 cm) and is field-drilled for maximum flexibility in each installation.



Sewage/Waste Junction Boxes

NEMA-4X Junction Boxes are electrical enclosures that are watertight, dust-tight, and corrosion resistant. Boxes are completely assembled with cord seals and terminal strip for easy field wiring.



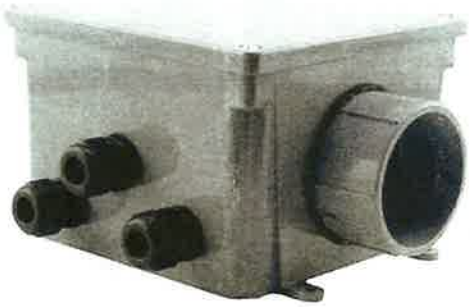

Deluxe Junction Box(Factory Assembled)

High-impact, corrosion-resistant, weatherproof thermoplastic enclosure with flexible PVC gasket and brass screws. Preassembled at the factory for convenience and ease of installation.

Qwik- Box Pump Control and Alarm

The Qwik-Box is a junction box designed for easy hookup of pumps and alarm systems. It is used in septic effluent, sewage, or dewatering applications, and requires a connection outside the building or residence. The Qwik-Box eliminates the need for junction wiring boxes inside sewage and septic tanks, and consists of UL listed components.

SPECIFICATIONS:

- No need to cut off plugs
- Sealed watertight enclosure
- Available in 115 Volt or 230 Volt design
- Corrosion-resistant PVC construction
- Easy hookup of indoor alarm with terminal strip exposed for low voltage wiring
- Rated for NEMA 4X
- Water-tight rubber cord seal for pump and switch cables
- Optional indoor tank alert alarm with silence switch and LED indicator
- Installation and wiring instructions included
- Meets NEC requirements for a disconnect

See FM1420 for further information.

Starter Kits

A starter kit is required for all single phase model 611, 621, 631, 641, and 651 pumps. A starter kit consists of the single phase capacitors and relay required to run the pump. These components are shipped loose and are installed into the pump's control panel.

Certified to CSA Standard 227875 | Tested to UL Standard UL778.

© All rights reserved.


SEPTIC PRODUCTS INC

CONTROL PANEL

50B137-NETFA Control Panel

Features & Benefits

- Circuit Breakers for Pump, Compressor & Alarm Circuits
- 24 Hr Timer w/15 minute intervals
- Large & Easy to Access Terminal Block
- Externally Mounted Run/Mute/Test Switch w/UV resistant sealing boot
- Externally Mounted Audible Alarm
- Rugged UV resistant Externally Mounted Alarm Light
- Durable Weather Resistant Hinged Poly Enclosure
- Silk Screen Back Panel
- Ground Lug
- Easily Replaceable Components
- Nema 4x Rating
- Color Coded Internal Wiring
- Built and Labeled to UL 508A Standard
- Works with most Aerobic Treatment Systems
- Provided with Wiring Schematic and Detailed Connection Diagram for Installer
- Mounting Feet for Enclosure

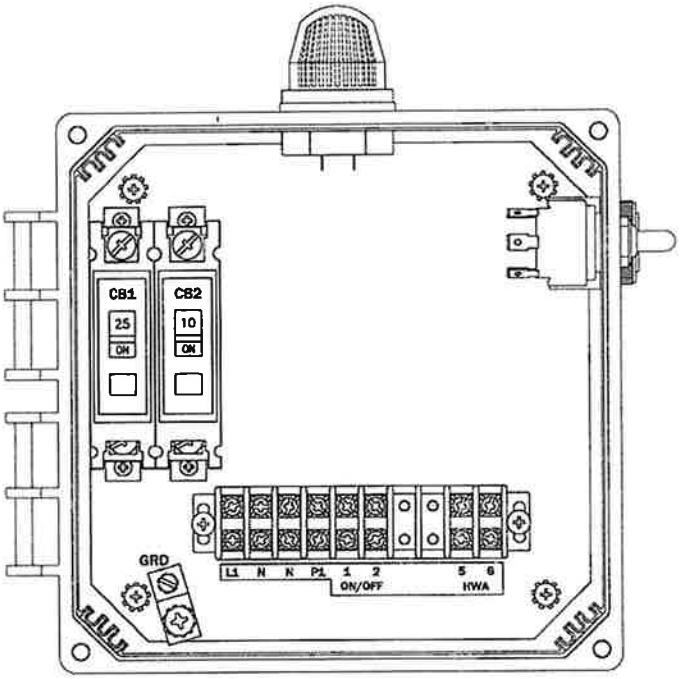

UL LISTED C UL

Available Options

- Externally Mounted Pump Test Switch
- Externally Mounted Air Pressure Switch
- Auto-Dialer
- Locking Stainless Steel Latch
- Repeat Cycle Timer Option
- Mercury or Mechanical Float Switches for the Pump and High Water Alarm Circuits

Note: Consult the factory for other available options. Also, some options may require an increase in the enclosure size.

Septic Products, Inc. 1378 Twp Rd Ashland, Ohio: (419)282-5933 Fax: (419)282-5943

Trusted. Tested. Tough.™

Product information presented here reflects conditions at time of publication. Consult factory regarding discrepancies or inconsistencies.

ZOELLER® PUMP COMPANY

SECTION: 2.15.080
FM2784
1017
Supersedes
0315

TECHNICAL DATA SHEET
DOSE-MATE SERIES
Models 151, 152, 153 Effluent Pumps


PRODUCT SPECIFICATIONS

MOTOR	Horse Power	1/3 (151), 4/10 (152), 1/2 (153)
	Voltage	115 or 230
	Phase	1 Ph
	Hertz	60 Hz
	RPM	3450
	Type	Permanent split capacitor
	Insulation	Class B
	Amps	3.0 - 10.5
PUMP	Operation	Automatic or nonautomatic
	Discharge Size	1-1/2" NPT
	Solids Handling	1/2" (12 mm), 3/4" (19 mm) spherical solids
	Cord Length	20' (6 m)
	Cord Type	UL listed power cord
	Max. Head	44' (13.4 m)
	Max. Flow Rate	77 GPM (291 LPM)
	Max. Operating Temp.	130 °F (54 °C)
	Cooling	Oil filled
	Motor Protection	Auto reset thermal overload
MATERIALS	Cap	Cast iron
	Motor Housing	Cast iron
	Pump Housing	Cast iron
	Base	Plastic or cast iron
	Upper Bearing	Sleeve bearing
	Lower Bearing	Ball bearing
	Mechanical Seals	Carbon and ceramic
	Impeller Type	Non-clogging vortex
	Impeller	Engineered thermoplastic
	Hardware	Stainless steel
	Motor Shaft	AISI 1215 steel
	Gasket	Neoprene


NOTE: The sizing of effluent systems normally requires variable level float(s) controls and properly sized basins to achieve required pumping cycles or dosing timers with nonautomatic pumps.

NOTE: See model comparison chart for specific details.

MODEL 151

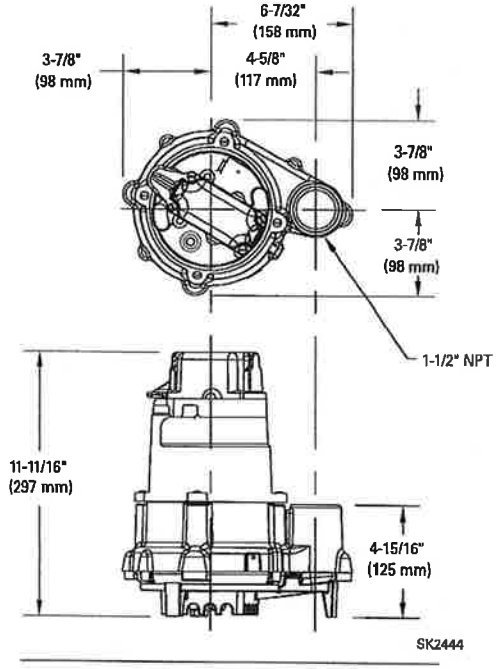

MODELS 152 & 153

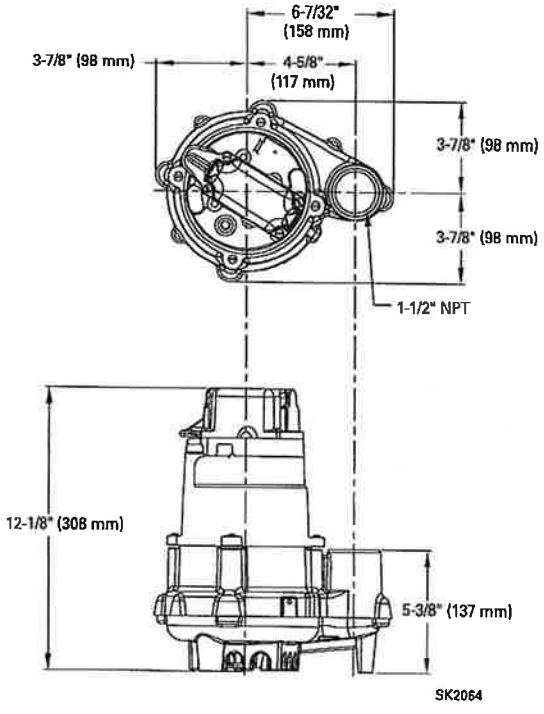


Tested to UL Standard UL778 and Certified to CSA Standard CSA22.2 No. 108

© Copyright 2017 Zoeller® Co. All rights reserved.

502-778-2731 | 800-928-7867 | 3649 Cane Run Road | Louisville, KY 40211-1961 | zoellerpumps.com

EZflow 1201P - GEO

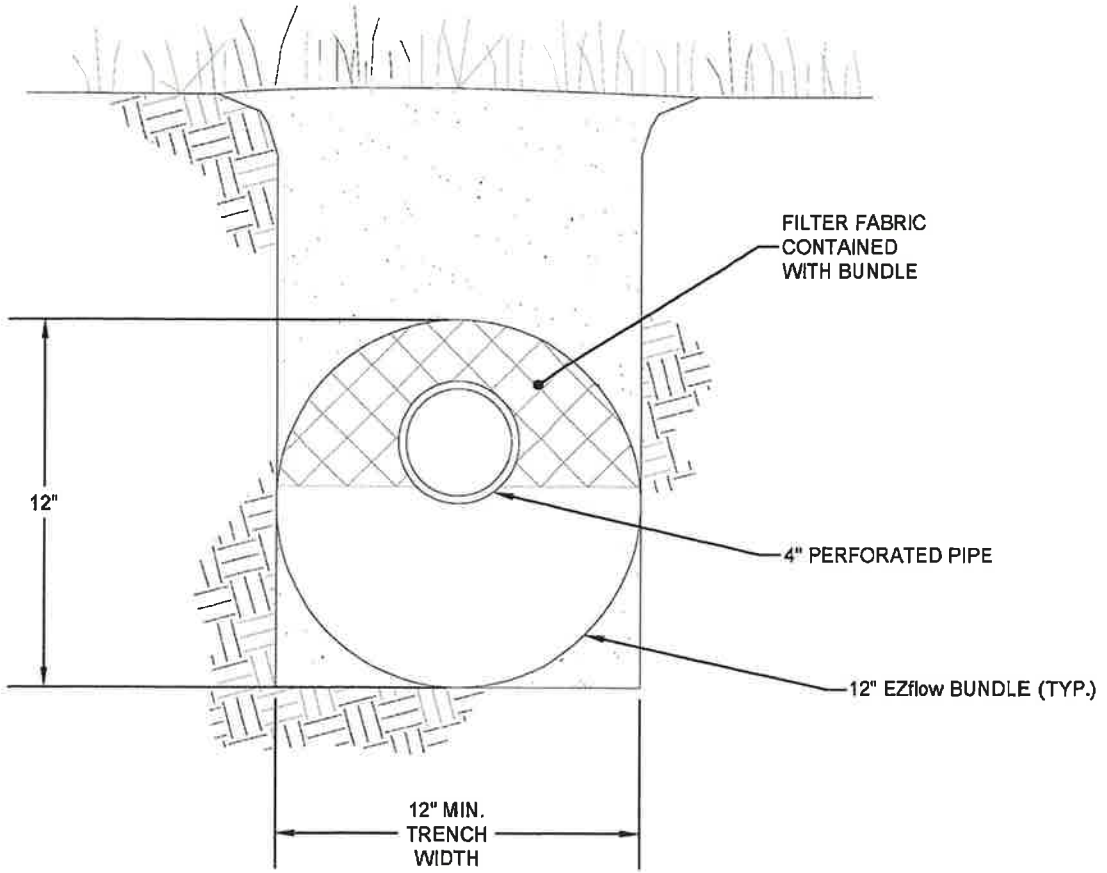

Infiltrator Water Technologies Part of ADS	EZflow	DRAWN BY: AG
		DATE: 04/15/2025
		SCALE: N/A
INFILTRATOR WATER TECHNOLOGIES, LLC 4 BUSINESS PARK RD, OLD SAYBROOK, CT 06475 WWW.INFILTRATORWATER.COM PHONE: (800) 221-4436 / EMAIL: INFO@INFILTRATORWATER.COM	EZflow 1201P - GEO TYPICAL CROSS SECTION DETAIL	SHEET NO.: 01 of 01

Quick4® Equalizer 24

Chambers

The Quick4 Equalizer 24 Chamber fits in a 18" wide trench and is ideal for curved or straight systems. It features the patent-pending Contour Swivel Connection™ which permits turns up to 10°, right or left. The MultiPort™ endcap allows multiple piping options and eliminates pipe fittings. The chamber's four-foot length provides optimal installation flexibility.



Quick4 Equalizer 24
MultiPort EndCap

IAPMO R&T

Benefits

- *Advanced contouring connections swivel up to 10°, right or* left
- Reinforced ribs provide increased structural capability and durability
- Compact nesting provides more trench length in an equivalent stack height
- Four-foot chambers are easy to handle and install
- The Quick4 Equalizer 24 Chamber supports wheel loads of 16,000 lbs/axle with only 12" of cover


Quick4 Equalizer 24 Chamber Specifications	
Size	16"W x 53"L x 11"H (406 mm x 1346 mm x 279 mm)
Effective Length	48" (1219 mm)
Louver Height	9.10" (231 mm)
Storage Capacity	21 gal (79 L)
Invert Height	6" (152 mm)

MultiPort Endcap Benefits:


- Tear-out seals on inlet ports provide a tight fit to the pipe
- Six molded-in inlets/outlets allow for maximum piping flexibility
- Fits on either end of the Quick4 Equalizer 24 Chamber
- MultiPort endcap fits on either end of the chamber

Contact Infiltrator's Technical Services Department for assistance at 1-800-221-4436 or info@infiltratorwater.com


Quick4 Equalizer 24 Chamber



Multiport Endcap



Typical Trench View




Quick4 EQ 24

Scan QR Code for Installation Instructions

Infiltrator Water Technologies
Part of ADS

fig. 9

Lateral Line Trench Detail

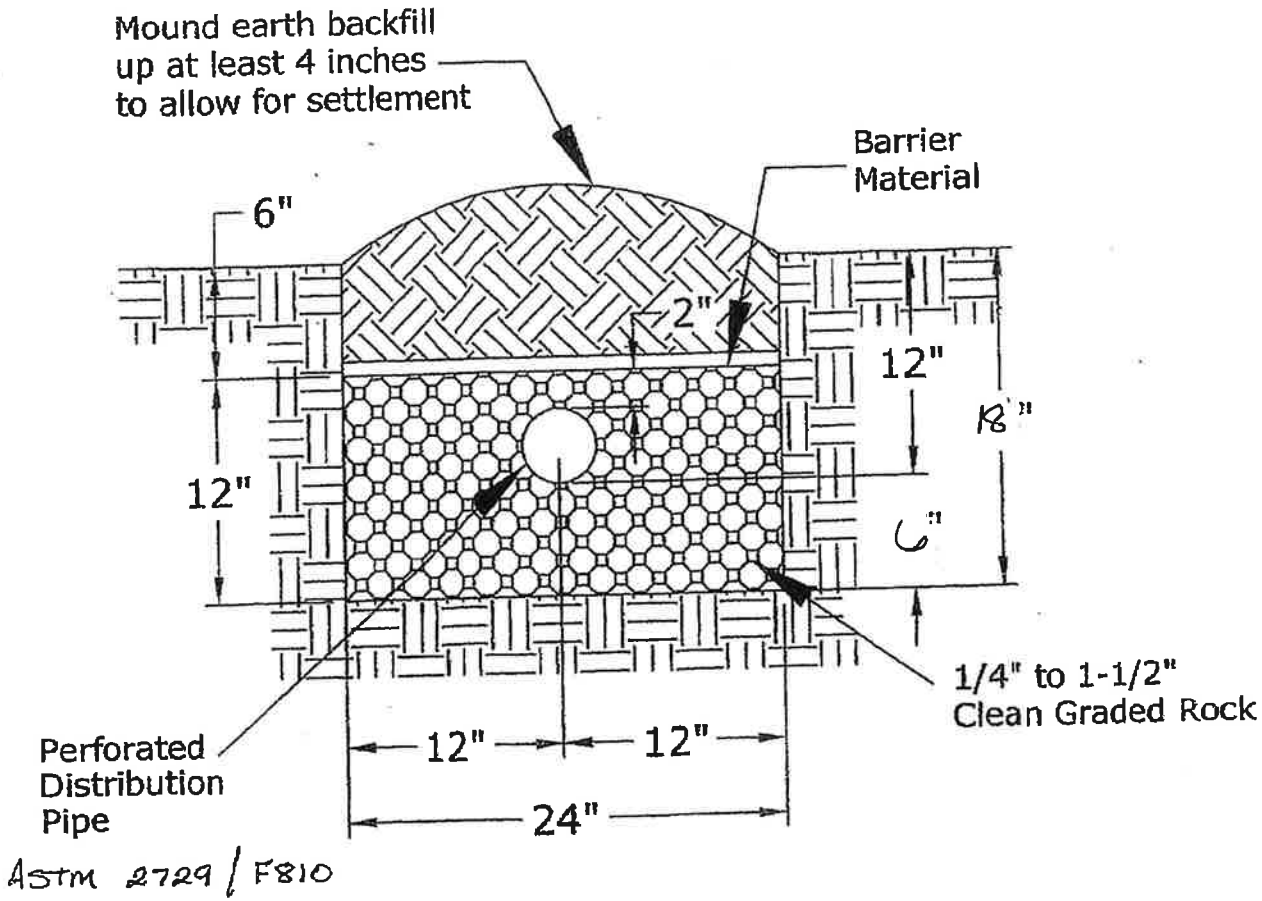


18" Trench Depth

GRANT BRANDON/SON HYE JIN
STEWART RD
LITTLE ROCK, AR 72211

Basic Information

Parcel Number:	54R0020700100
County Name:	Pulaski County
Property Address:	GRANT BRANDON/SON HYE JIN STEWART RD LITTLE ROCK, AR 72211 Map This Address
Mailing Address:	GRANT BRANDON/SON HYE JIN 30 WILDWOOD PLACE CIR LITTLE ROCK AR 72223-8002
Total Acres:	4.76
Timber Acres:	0.00
Sec-Twp-Rng:	02-1N-14W
Lot/Block:	1/
Subdivision:	KENNEDY ESTATES
Legal Description:	LOT 1, KENNEDY ESTATES
School District:	011 PCSSD SOUTH OF RIVER
Improvement Districts:	WEST PULASKI FIRE,WEST KANIS/DENNY RD WATER
Homestead Parcel?:	No
Tax Status:	Taxable
Over 65?:	No

Parcel Boundary

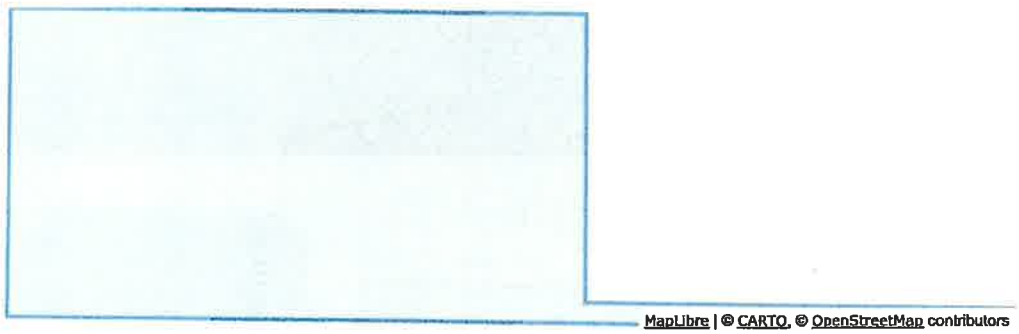

Land Information

Land Type	Quantity	Front Width	Rear Width	Depth 1	Depth 2	Quarter
RA40000	4.76 acres [207,346 sqft]					

Valuation Information — view prior year information

Entry	Appraised	Assessed
Land:	190,400	38,080
Improvements:	0	0
Total Value:	190,400	38,080
Taxable Value:		38,080
Millage:		0.0508
Estimated Taxes:		$1,934.46
Assessment Year:		2026

Sales History

Google Maps 510 Stewart Rd



Imagery ©2026 Airbus, Maxar Technologies, Map data ©2026 Google 100 ft



510 Stewart Rd

Directions Save Nearby Send to phone Share

510 Stewart Rd, Little Rock, AR 72223

QG5F+GR Little Rock, Arkansas
